


Republic Road Project Update



US Army Corps of Engineers

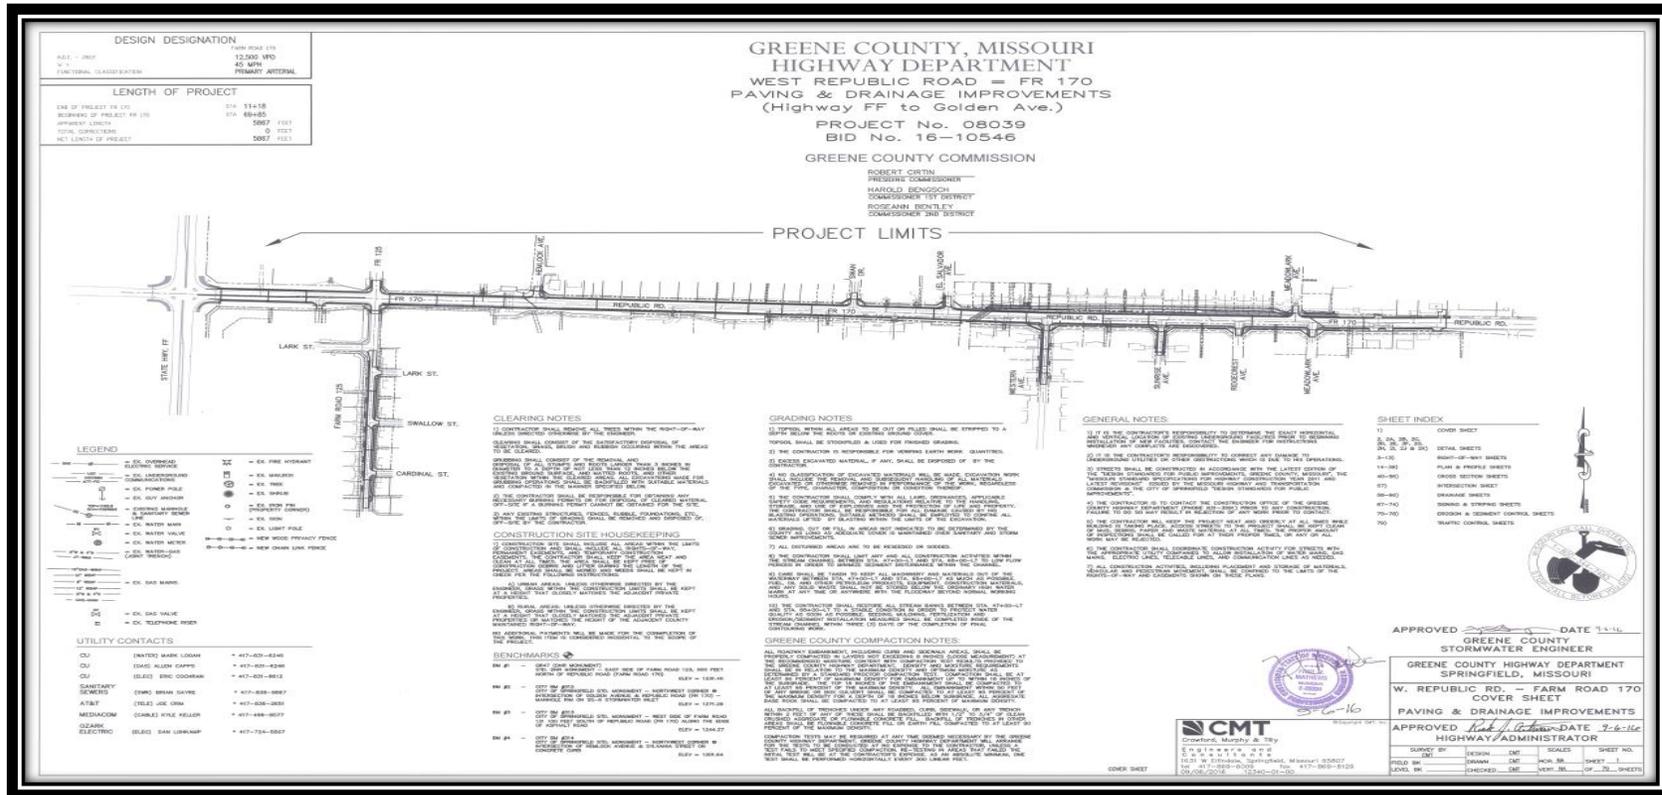

US Army Corps of Engineers

- Applied for Permit - July 2015
- Jurisdictional Determination - October 2015




US Army Corps
of Engineers®

“ Relatively Permanent Waters (RPW) that flow indirectly to a Traditional Navigable Waterway.”

US Army Corps of Engineers

- Original Application Date - July 2015
- Permit Received by County - December 2016
- 18 Month Project Delay
- Total Mitigation Fee = \$88,000 (to the Missouri Stream Stewardship Trust Fund)

Republic Road Project Bidding:



- Original Bid Date - September 16, 2015
 - Low Bidder = \$5.88 million
- 2nd Bid Date - October 11, 2016
 - Low Bidder = \$5.50 million


SAVINGS OF
\$380K

Republic Road Project Construction:

- Construction Start Date - January 2017
- 18-Month Construction Contract
- Completion Deadline - July 2018
- Prime Contractor - Hartman Construction

Republic Road Project Construction:


- Construction Start Date - January 2017
- 18-Month Construction Contract
- Completion Deadline - July 2018
- Prime Contractor - Hartman Construction

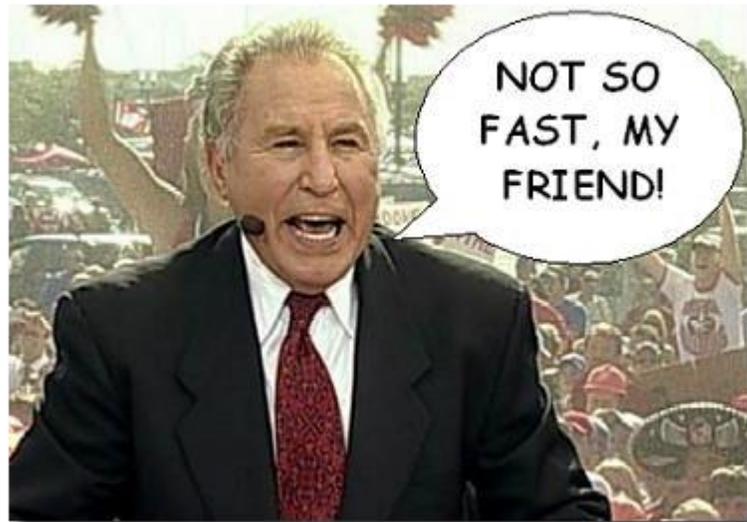

Republic Road Project Construction:



We have a problem....



Republic Road Project Construction:



Republic Road Project Construction:



Republic Road Project Construction:



Republic Road Project Construction:

ROAD CLOSURE COMING...

- September 5th thru October 14th

